Figure 2.0-24
Preliminary Project Schedule

ID	Task Name	Start	Finish
1	**Key Milestones**	**Mon 3/4/02**	**Mon 5/31/04**
2	Power Island Equip. Released	Mon 3/4/02	Mon 3/4/02
3	EPC Limited Notice to Proceed	Mon 6/3/02	Mon 6/3/02
4	Full Notice to Proceed	Mon 7/22/02	Mon 7/22/02
5	Receive Permits	Thu 7/18/02	Thu 7/18/02
6	Commence Site Mobilization - EPC	Mon 7/29/02	Mon 7/29/02
7	Receive CTG#1 F/F	Fri 11/8/02	Fri 11/8/02
8	Receive CTG#2 F/F	Fri 11/15/02	Fri 11/15/02
9	Receive STG F/F	Mon 3/10/03	Mon 3/10/03
10	Mechanical Completion	Fri 12/12/03	Wed 12/17/03
11	1st Fire - CTG #1	Fri 1/16/04	Fri 1/16/04
12	1st Fire - CTG #2	Fri 2/13/04	Fri 2/13/04
13	1st Synchronization-STG	Fri 3/26/04	Fri 3/26/04
14	Commercial Operation	Mon 5/31/04	Mon 5/31/04
15			
16	**Engineering**	**Mon 3/18/02**	**Fri 9/19/03**
17	Detailed Geotechnical Studies	Mon 3/18/02	Fri 5/24/02
18	G/A's, Grading, Drainage	Mon 6/17/02	Fri 10/4/02
19	Foundation Design	Mon 8/12/02	Fri 3/21/03
20	Major Equipment Specs.	Mon 6/24/02	Fri 4/4/03
21	Building/Structure Design	Mon 9/9/02	Fri 3/21/03
22	Mechanical Design	Mon 8/5/02	Fri 7/25/03
23	Electrical Design	Mon 8/26/02	Fri 8/22/03
24	I&C Design	Mon 9/16/02	Fri 9/19/03
25			
26	**Purchase/Fabrication**	**Mon 3/11/02**	**Fri 3/28/03**
27	CTG's	Mon 3/11/02	Fri 3/14/03
28	STG	Mon 3/25/02	Fri 3/28/03
29	Condenser	Mon 7/8/02	Mon 3/3/03
30	HRSG's	Mon 4/15/02	Fri 1/17/03
31	Balance of Plant	Mon 7/29/02	Fri 1/24/03
32			
33	**Construction**	**Mon 6/3/02**	**Fri 12/5/03**
34	Owner's Pre-mobilization Activities	Mon 6/3/02	Mon 7/8/02
35	Mobilize & Site Prep	Mon 7/29/02	Fri 9/13/02
36	Foundations	Mon 8/12/02	Fri 4/25/03
37	Steel Structure-Bldgs	Mon 12/9/02	Fri 4/25/03
38	Erect CTG's	Fri 10/25/02	Fri 8/22/03
39	Erect STG/Condenser	Mon 3/3/03	Fri 12/5/03
40	Erect HRSG's	Mon 11/11/02	Fri 11/7/03
41	Erect BOP Equipment	Mon 12/16/02	Fri 10/17/03
42			
43	**Commissioning**	**Fri 9/12/03**	**Mon 5/31/04**
44	Electrical/I&C Checkout	Mon 10/6/03	Fri 3/5/04
45	Hydros & Flushes	Mon 9/22/03	Fri 2/13/04
46	230 KV Backfeed	Fri 10/17/03	Fri 10/17/03
47	Water Supply/Return Systems Available	Fri 9/12/03	Fri 9/12/03
48	1st Fire	Fri 1/9/04	Fri 1/9/04
49	Clean Steam Cycle	Fri 1/23/04	Fri 2/27/04
50	Combined Cycle Comm.	Fri 2/20/04	Fri 5/21/04
51	Performance & Emissions Testing	Mon 5/17/04	Fri 5/28/04
52	Commercial Operation	Mon 5/31/04	Mon 5/31/04
53			
54	**Gas Interconnect**	**Mon 11/18/02**	**Fri 8/29/03**
55	Design	Mon 11/18/02	Fri 2/14/03
56	Procurement/Fab	Mon 1/6/03	Fri 4/25/03
57	Construction	Mon 5/19/03	Fri 7/25/03
58	Commissioning	Mon 8/4/03	Fri 8/29/03
59			
60	**Bulk Blvd Upgrade & Plant Interconnect**	**Mon 6/3/02**	**Fri 10/10/03**
61	Prepare/Execute Contracts w/Western	Mon 6/3/02	Fri 7/12/02
62	Design	Mon 7/22/02	Fri 2/7/03
63	Procurement/Fab	Mon 8/19/02	Fri 5/9/03
64	Construction	Mon 4/14/03	Fri 9/12/03
65	Commissioning	Fri 8/22/03	Fri 10/10/03

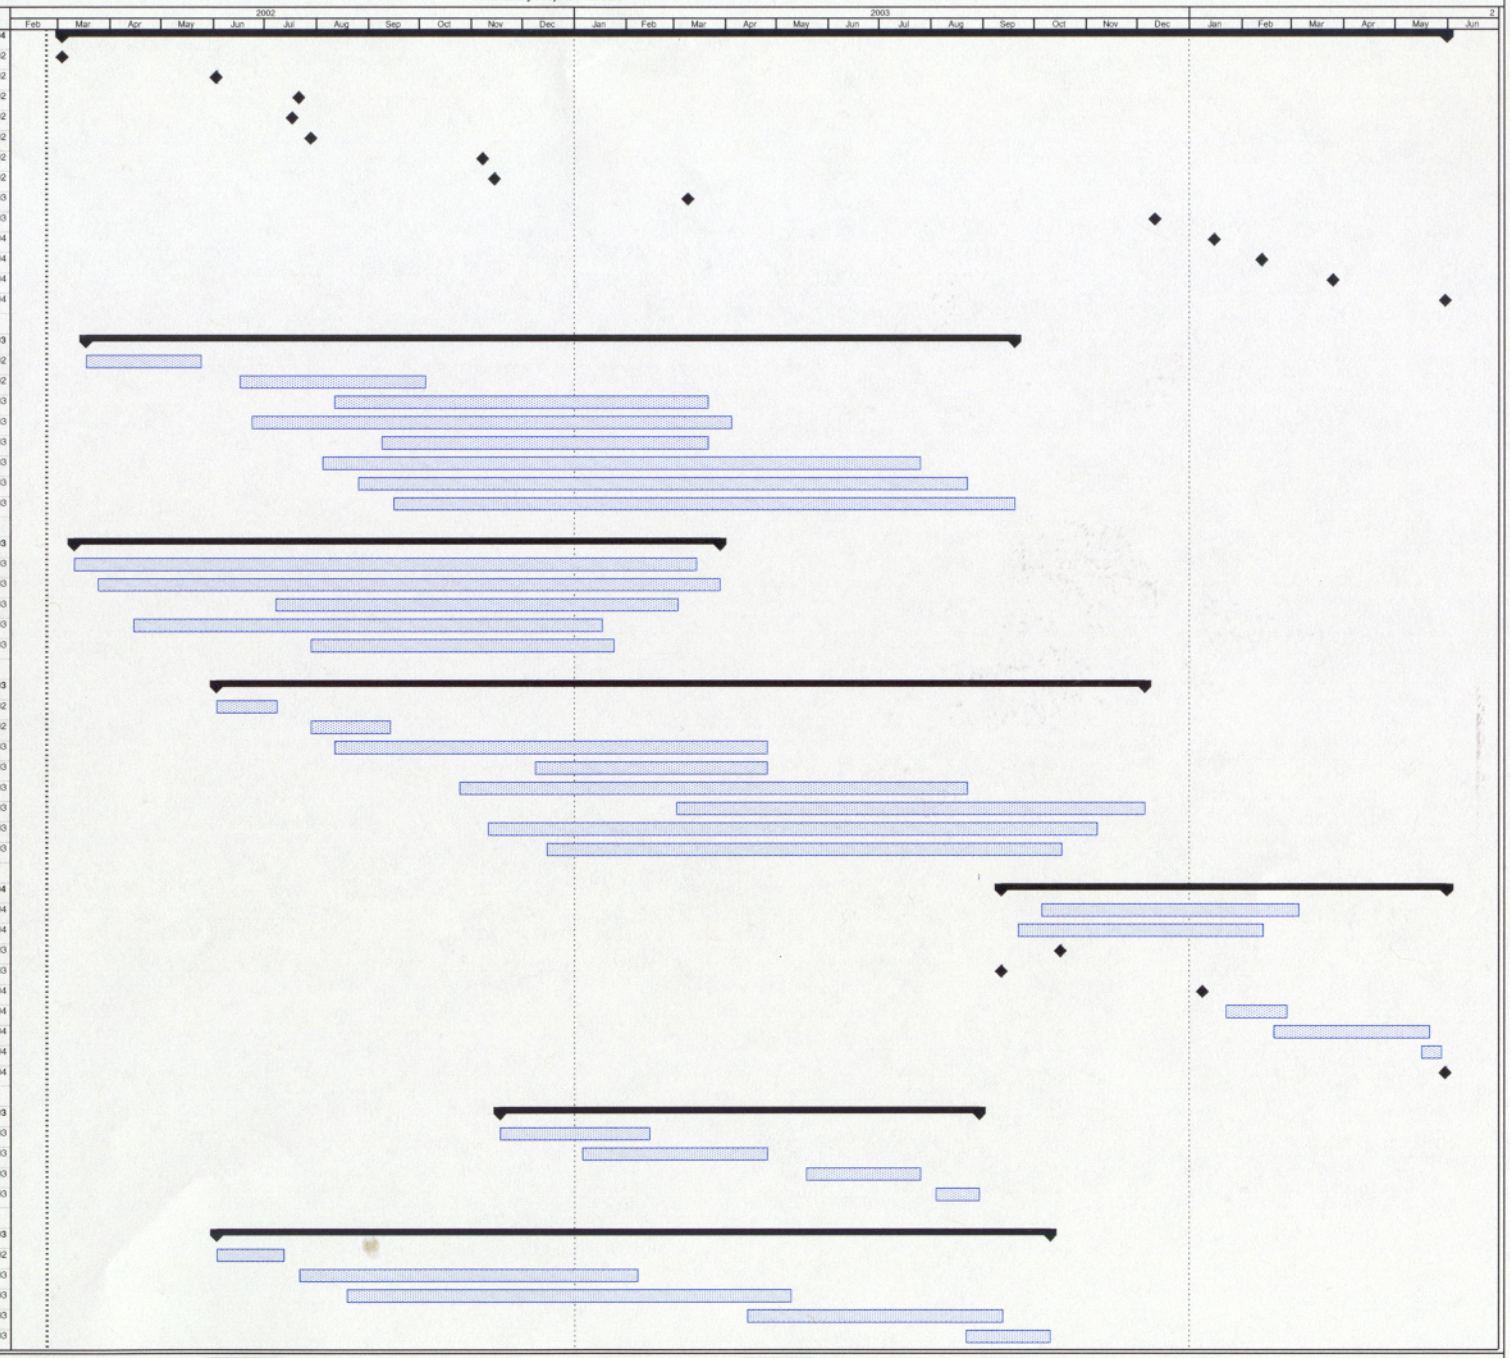

Project:Blythe Energy Project-Phase II
Date: Fri 2/22/02

Task | Progress | Summary | Rolled Up Split | Rolled Up Progress | Project Summary | Deadline
Split | Milestone | Rolled Up Task | Rolled Up Milestone | External Tasks | External Milestone
